

DESIGN AND CONSTRUCTION UPDATE



DESIGN DEVELOPMENT

Tunnel Inlet to Houston Street

- February 28: Final design documents were submitted for pricing
- April 27: Price proposal from SDJV for remainder of scope



DESIGN DEVELOPMENT

Tunnel Inlet to Houston Street

- Ongoing coordination between design team and SDJV for interpretive art elements
 - Artists engagement
 - Design and construction coordination
 - Material selection and procurement
- Schedule of presentations on art elements to Commissioners Court revised
- Coordination with Plethora art team ongoing



DESIGN DEVELOPMENT


Phase 1 South of Houston and Phase 2

- Concerns over the ability to meet May 19 90% design deliverable date
- Still working on components from inlet to Houston
 - Completion of remaining components of the interpretive plan
 - Delays in advancement of other design elements
 - Landscape architect leaving team
- Coordination with design team to mitigate delays



CONSTRUCTION ACTIVITIES


- Utility Relocations on Nueva and Houston
- CPS relocations between Martin and Santa Rosa

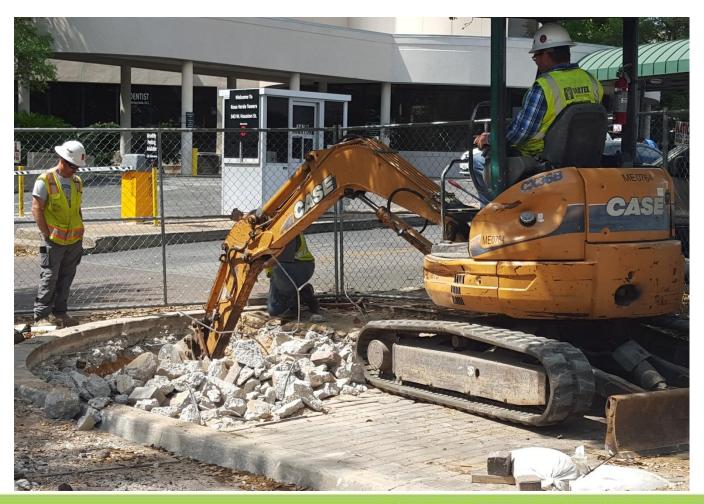



CONSTRUCTION ACTIVITIES


- Installation of new storm drain infrastructure and equalizer piping at the tunnel inlet
- Drilled Shafts
- Sewer Relocation

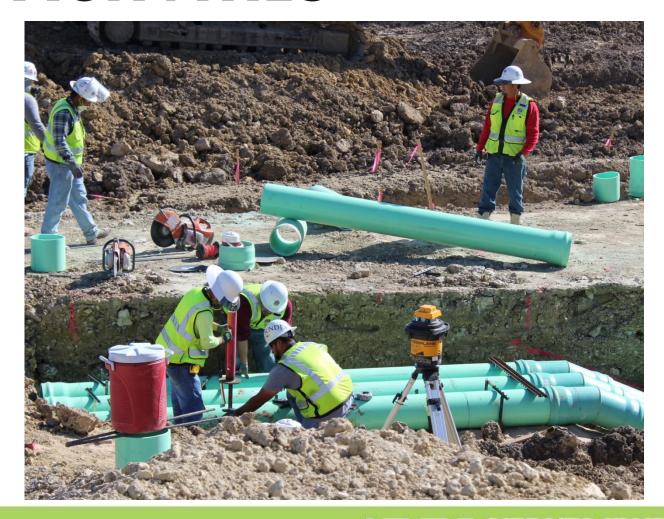




CONSTRUCTION ACTIVITIES

 Demolition of Salinas Street Bridge

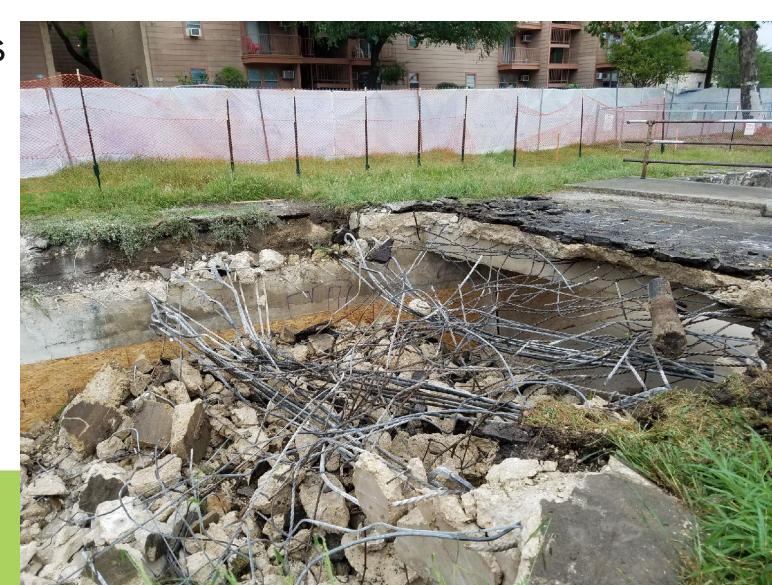

CURRENT STREET CLOSURES

- North Santa Rosa Street between
 West Martin and San Saba Streets.
- Houston Street from Laredo Street to Camaron Street is closed and the westbound lane of Houston Street from Flores Street to Camaron Street.
- Camaron Street from Houston Street to the Santa Rosa Street Bridge is closed.

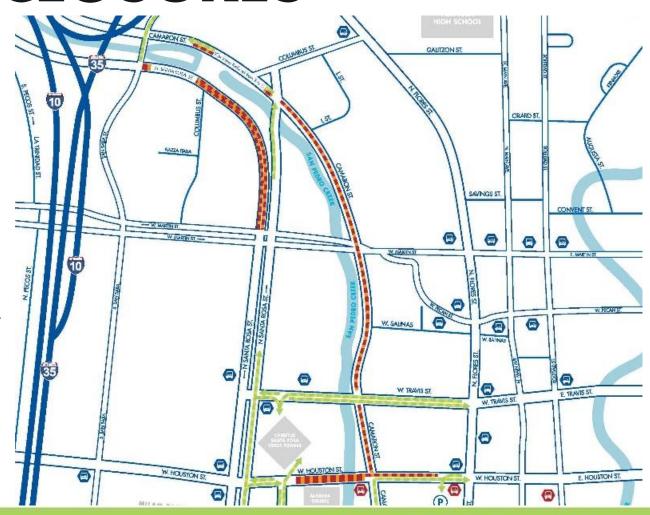




FIESTA STREET CLOSURES

• Eastbound Houston Street will reopen.

- Camaron Street closure will remain.
- Houston and Dolorosa Streets fully open.

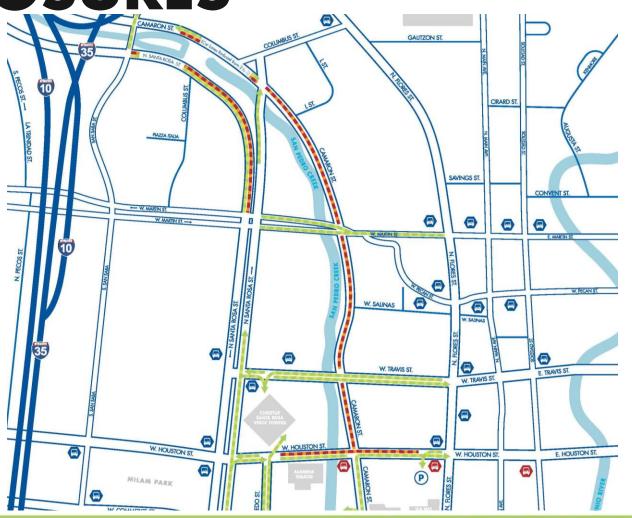



UPCOMING STREET CLOSURES

- Commerce Street and Dolorosa Street
 - 2 lane closures for utility relocations beginning after Fiesta




PROJECTED STREET CLOSURES

- Full closure of Commerce Street: November 2017 for 3 months
 - Houston Street will be fully opened during the full closure of Commerce Street
- Projected closures of other street bridges in Phases 1 & 2 approved by COSA
 - Schedule being generated



CONSTRUCTION TOURS

- Media and Elected Officials: March 30
- Public Tour: March31
- Next Public Tour:
 June 2
- Possible separate tour for the Subcommittee

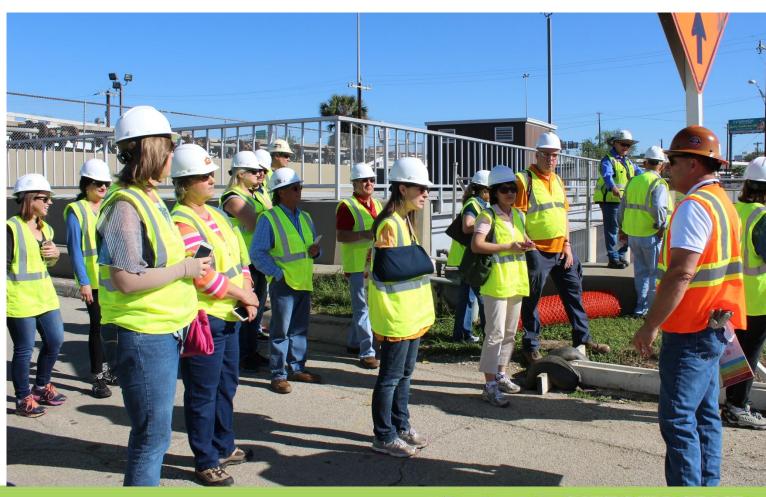



UPCOMING CONSTRUCTION ACTIVITIES

- Complete utility work on Nueva Street
- Continue utility work on Houston and Dolorosa Streets
- Construction of walls and planters at the inlet structure
- Begin excavation between Santa Rosa and Martin Streets



OTHER ACTIVITIES

- Promotion of San Pedro Creek businesses
- Presentation to Commissioners Court: April 18
- Presentation tour schedule
- Distribution of Fiesta Medals
- Distribution of Art Plans



